

Scott Hedlund

From: Scott Hedlund
Sent: Thursday, June 12, 2025 6:13 PM
To: Scott Hedlund
Subject: From the City of Sauk Rapids - 2025 Overlay and 2025 Highview Area project - Project Update – June 12, 2025

Residents and Project Stakeholders:

This is the first email update for the 2025 Overlay and 2025 Highview Area Street & Utility Improvements project. The intent of the updates is to notify residents and other interested parties of recent and upcoming work, and to provide relevant details related to the construction activity. Please pass along this update to others in your home or adjacent residents and encourage them to provide email address to me to get added to this distribution list. For reference, the first and only mailed project update was sent to adjacent property owners the first week of June. All subsequent project updates will be sent by email only with copies available on the project website (address below).


The project team would like to thank you for your patience as we near the start of construction of this project. Feel free to continue to contact SEH with any questions or concerns regarding the project. We hope to respond in a timely manner. However, when more than one team member needs to be consulted, it may take a little longer to provide you with accurate up-to-date information.

Jeff Supan, SEH's Field Representative, will be on-site during active construction to observe project progress (and has been out on site the last couple of weeks marking concrete removals – drives a black Toyota Highlander). He is the fastest link to problem solving because he communicates directly with everyone on the construction team. Do not hesitate to contact Jeff at 320.250.3381 with any questions you may have. If you are unable to reach Jeff in the field, please contact Scott Hedlund at 612.865.3509 in the SEH office.

Project Schedule/ Upcoming Work:

The City's Contractor is gearing up to begin construction and has given the following updated major milestones, primarily in reference to start dates, subject to change and the weather:

- Weeks of June 23rd, June 30th, and July 7th:
 - **Begin construction in the Overlay portion of the project on June 23rd in the Garden Brook, Stone Ridge, and Oak Crest neighborhoods** to include:
 - Targeted concrete curb, sidewalk, and pedestrian curb ramp replacements.
 - Casting replacements and adjustments.
 - Targeted storm pipe/culvert repairs.

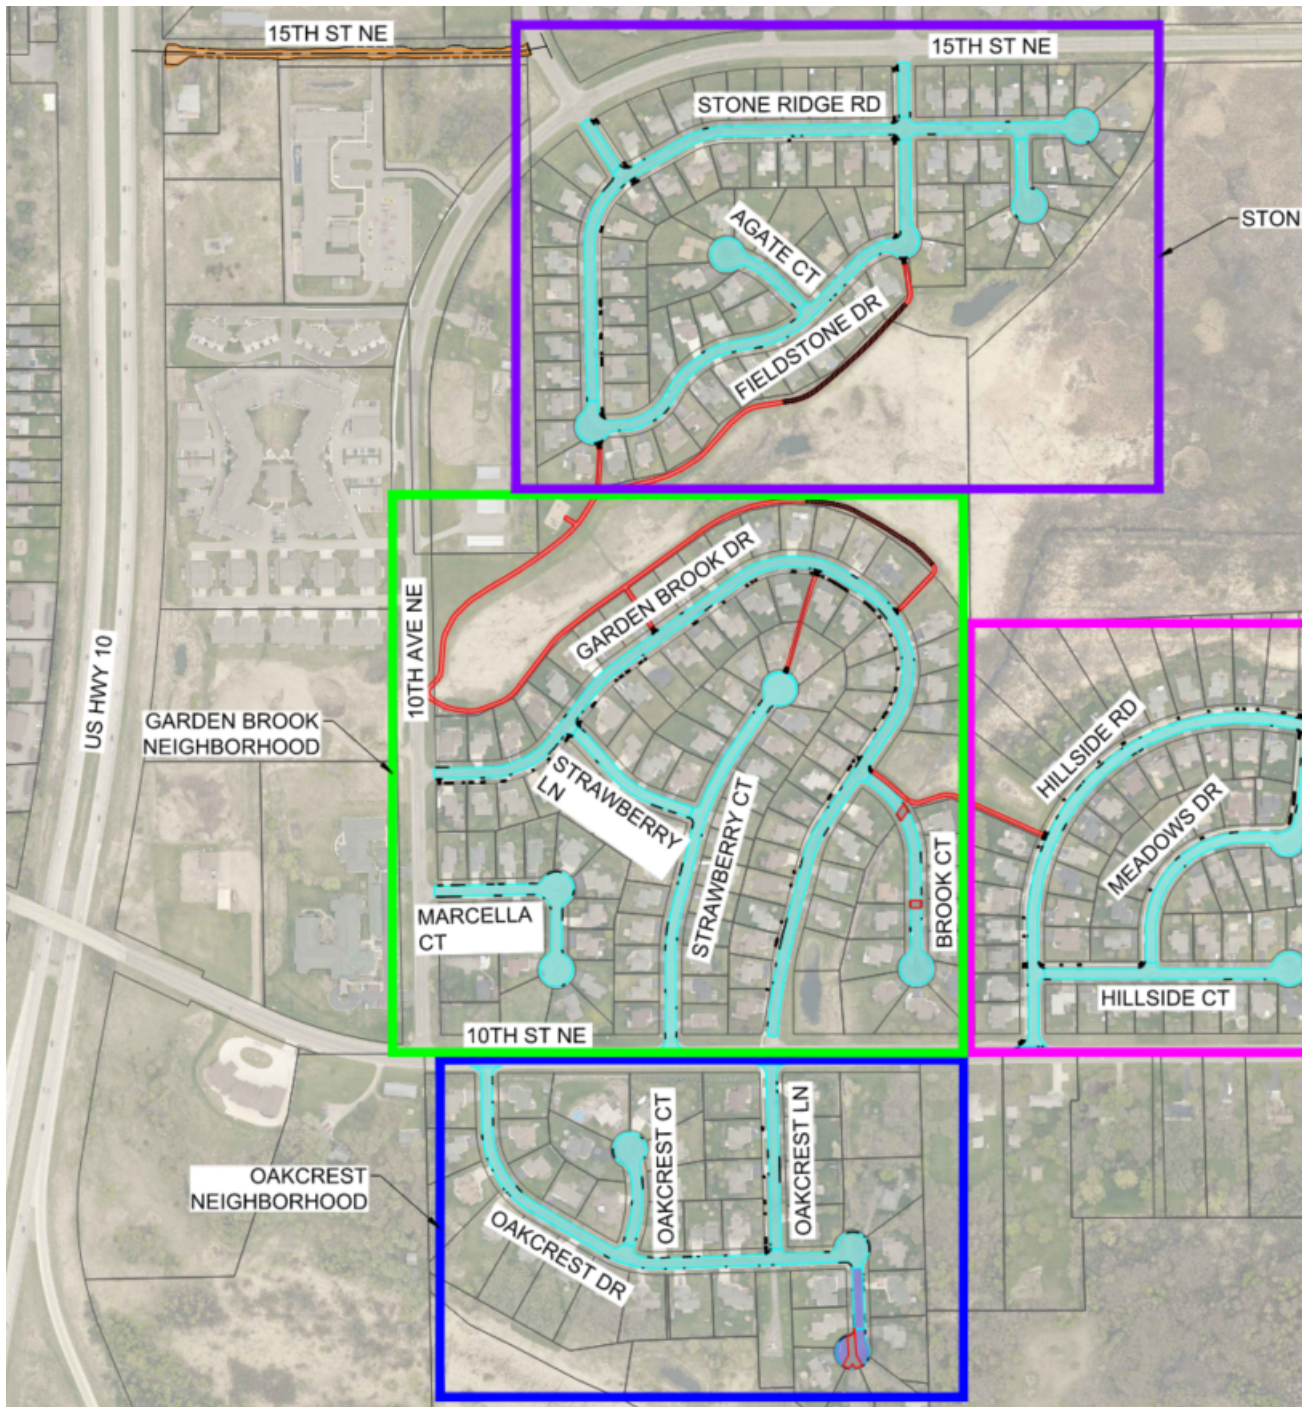

- Week of July 14th:
 - **Begin construction in the Highview Area of the project on or about July 14th starting with:**
 - Water main work on North Highview Drive between East Highview Drive and Oak Drive including at the intersections (**Note, this is the only planned water main work on the entire project**).
 - Associated pavement removals to facilitate the work
- Construction is planned to be completed in 2025 by the end of September, weather permitting, subject to change.

Please remember that construction schedules can change at a moment's notice because of weather, delays by subcontractors, or other unforeseen events.

Special Information:

It is very important that anyone with special needs or disabilities contact us as soon as possible. We are in the process of working with emergency response organizations to locate any residences that may have a special need, so we are fully aware of the issues throughout construction and if quick response is needed to any specific residence(s), there is a plan in place. Contact Jeff Supan with SEH at 320.250.3381.

Private Utility Work:

Within the Highview Area portion of the project there has been and will be some additional private utility relocation work completed in the coming weeks. Xcel Energy natural gas crews recently completed relocating a main and services ahead of the planned water main work along North Highview Drive and Oak Drive. Xcel Energy electric crews will be relocating a power pole in the southwest corner of the West Highview Drive/ High Drive intersection. Note, **the City of Sauk Rapids does not control the activities and operations of the private utility companies.**

24-hour Emergency Contact:

If you need assistance related to access or other construction related problems, the primary contact from **Knife River Corporation – North Central** is **Matt Otremba, phone number (320)-630-9963.**

Access Limited in Areas of Utility and Concrete Work:

During the water main and storm pipe repair work there will be temporary access restrictions to properties in the immediate vicinity of that work. When crews are working on your street, the intent is for vehicles to be able to leave in the early morning, and return in the evening, but access restrictions during the daytime working hours may occur. **Project staff will coordinate with residents to alert them of access restrictions.**

If any concrete (curb & gutter or sidewalk) repair work crosses your driveway, it will not be vehicle-accessible when the concrete is being formed, poured, and curing. Concrete can take up to 7 days to properly cure prior to driving a vehicle on it. Property owners with impacted driveways will need to park on the street during this time.

Please refrain from on-street parking within the project limits during daylight hours until further notice (unless you are unable to utilize your driveway due to project concrete repair work).

Work Zones:

Notice on Construction Zone Activities:

- **The majority of the City Contractor's work within roadway corridors is planned to be completed under traffic.**
- It is necessary to close the trails in order complete the resurfacing work.
- Road & trail work signs, other temporary signage, and or flaggers will be in place in the project areas to warn motorists & pedestrians, and protect workers during construction. Please pay careful attention to the warning signs and flaggers. Please exercise caution as you navigate the work zones.

Project Website:

Please note the link below, which includes information about the project.

Link: <https://www.sehinc.com/2025overlayhighview>

Thank you,

Scott D. Hedlund, PE (MN, LA), PMP

Sauk Rapids City Engineer

Principal, Project Manager

Short Elliott Hendrickson, Inc.

612.865.3509 mobile

Building a Better World for All of Us®

Follow [SEH](#) on [Twitter](#) | [Facebook](#) | [LinkedIn](#) | [Instagram](#)
